

WILD ABOUT PONDS
(SITA Project No.4770)

ID	Task Name	Duration	Start	Finish	Pred	2010				2011				2012				2013			
						Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1		
1	WILD ABOUT PONDS (SITA)	790 days	Fri 01/01/10	Fri 18/01/13																	
2	MANAGEMENT PLANS	711 days	Thu 01/04/10	Fri 28/12/12																	
3	Dale Road Park (Spondon)	195 days	Mon 02/04/12	Fri 28/12/12																	
4	Site Survey	13 wks	Mon 02/04/12	Fri 29/06/12																	
5	Management Plan	13 wks	Mon 01/10/12	Fri 28/12/12	4FS+1																
6	Elm Wood LNR	159 days	Mon 02/05/11	Thu 08/12/11																	
7	Site Survey	19 wks	Mon 02/05/11	Fri 09/09/11	100																
8	Management Plan	12.8 wks	Mon 12/09/11	Thu 08/12/11	7																
9	Alvaston Park	116 days	Fri 01/07/11	Fri 09/12/11																	
10	Site Survey	10.2 wks	Fri 01/07/11	Fri 09/09/11	106																
11	Management Plan	13 wks	Mon 12/09/11	Fri 09/12/11	10																
12	Arboretum Park	130 days	Mon 02/07/12	Fri 28/12/12																	
13	Site Survey	13 wks	Mon 02/07/12	Fri 28/09/12	113																
14	Management Plan	13 wks	Mon 01/10/12	Fri 28/12/12	13																
15	Derby Moor School	130 days	Mon 02/07/12	Fri 28/12/12																	
16	Site Survey	13 wks	Mon 02/07/12	Fri 28/09/12	119																
17	Management Plan	13 wks	Mon 01/10/12	Fri 28/12/12	16																
18	Chellaston Brickworks (x4)	296 days	Mon 12/04/10	Mon 30/05/11																	
19	Site Survey (Amphibians)	1 day	Mon 12/04/10	Mon 12/04/10																	
20	Site Survey (PSYM)	1 day	Tue 01/06/10	Tue 01/06/10	19																
21	Management Plan	51.8 wks	Wed 02/06/10	Mon 30/05/11	20																
22	Allestree Park (x2)	314 days	Thu 01/07/10	Tue 13/09/11																	
23	Site Survey	9 wks	Thu 01/07/10	Wed 01/09/10	126																
24	Management Plan	53.8 wks	Thu 02/09/10	Tue 13/09/11	23																
25	Chaddesden Wood (x4)	116 days	Fri 01/07/11	Fri 09/12/11																	
26	Site Survey	10.2 wks	Fri 01/07/11	Fri 09/09/11																	
27	Management Plan	13 wks	Mon 12/09/11	Fri 09/12/11	26																
28	Da Vinci School (Chaddesden)	184 days	Thu 01/07/10	Tue 15/03/11																	
29	Site Survey	9 wks	Thu 01/07/10	Wed 01/09/10	149																
30	Management Plan	27.8 wks	Thu 02/09/10	Tue 15/03/11	29																
31	Education Pond (Alvaston)	330 days	Mon 19/04/10	Sat 23/07/11																	
32	Site Survey (Amphibians)	1 day	Mon 19/04/10	Mon 19/04/10																	
33	Site Survey (PSYM)	1 day	Tue 01/06/10	Tue 01/06/10	32																
34	Management Plan	59.6 wks	Wed 02/06/10	Sat 23/07/11	33																
35	Markeaton Mill	191 days	Fri 01/04/11	Sat 31/12/11																	
36	Site Survey	13 wks	Fri 01/04/11	Thu 30/06/11																	
37	Management Plan	13 wks	Fri 01/07/11	Sat 31/12/11	36																
38	Markeaton Park Wood	130 days	Mon 02/07/12	Fri 28/12/12																	
39	Site Survey	13 wks	Mon 02/07/12	Fri 28/09/12																	
40	Management Plan	13 wks	Mon 01/10/12	Fri 28/12/12	39																
41	Porters Lane (Oakwood)	172 days	Fri 06/08/10	Mon 04/04/11																	
42	Site Survey	1 day	Fri 06/08/10	Fri 06/08/10																	
43	Management Plan	34.2 wks	Mon 09/08/10	Mon 04/04/11	42																










Project: Project Plan v1.0R
Date: Mon 12/12/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

WILD ABOUT PONDS
(SITA Project No.4770)

ID	Task Name	Duration	Start	Finish	Pred	2010				2011				2012				2013
						Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
44	Starflower Waye (Mickleover)	160 days	Wed 21/04/10	Tue 30/11/10														
45	Site Survey (Amphibians)	1 day	Wed 21/04/10	Wed 21/04/10														
46	Site Survey (PSYM)	1 day	Tue 01/06/10	Tue 01/06/10	45													
47	Management Plan	26 wks	Wed 02/06/10	Tue 30/11/10	46													
48	Sinfin Golf	195 days	Thu 01/04/10	Wed 29/12/10														
49	Site Survey	13 wks	Thu 01/04/10	Wed 30/06/10														
50	Management Plan	13 wks	Thu 30/09/10	Wed 29/12/10	49FS+													
51	Sinfin Moor (x4)	160 days	Mon 26/04/10	Fri 03/12/10														
52	Site Survey (Amphibians)	1 day	Mon 26/04/10	Mon 26/04/10														
53	Site Survey (PSYM)	1 day	Tue 01/06/10	Tue 01/06/10	52													
54	Management Plan	26.6 wks	Wed 02/06/10	Fri 03/12/10	53													
55	Spondon Gilbert (x2)	256 days	Fri 01/04/11	Mon 02/04/12														
56	Site Survey	38.2 wks	Fri 01/04/11	Fri 23/12/11														
57	Management Plan	13 wks	Tue 03/01/12	Mon 02/04/12	56													
58	Sunnydale Park	130 days	Mon 02/04/12	Fri 28/09/12														
59	Site Survey	13 wks	Mon 02/04/12	Fri 29/06/12	218													
60	Management Plan	13 wks	Mon 02/07/12	Fri 28/09/12	59													
61	West Park Meadow (Spondon)	321 days	Mon 05/04/10	Mon 27/06/11														
62	Site Survey (Amphibians)	1 day	Mon 05/04/10	Mon 05/04/10														
63	Site Survey (PSYM)	1 day	Tue 01/06/10	Tue 01/06/10	62													
64	Management Plan	55.8 wks	Wed 02/06/10	Mon 27/06/11	63													
65	Chaddesden Park	423 days	Thu 01/04/10	Mon 14/11/11														
66	Site Survey	13 wks	Thu 01/04/10	Wed 30/06/10														
67	Management Plan	45.6 wks	Thu 30/12/10	Mon 14/11/11	66FS+													
68	Chaddesden Sidings (x3)	170 days	Thu 01/07/10	Wed 23/02/11														
69	Site Survey	9 wks	Thu 01/07/10	Wed 01/09/10														
70	Management Plan	12 wks	Thu 02/12/10	Wed 23/02/11	69FS+													
71	City Hospital	260 days	Fri 01/04/11	Fri 06/04/12														
72	Site Survey	13 wks	Fri 01/04/11	Thu 30/06/11														
73	Management Plan	13 wks	Mon 09/01/12	Fri 06/04/12	72FS+													
74	Derwent Valley (x2)	130 days	Mon 02/04/12	Fri 28/09/12														
75	Site Survey	13 wks	Mon 02/04/12	Fri 29/06/12														
76	Management Plan	13 wks	Mon 02/07/12	Fri 28/09/12	75													
77	Mickleover Meadows (x2)	181 days	Fri 01/07/11	Mon 19/03/12														
78	Site Survey	10.2 wks	Fri 01/07/11	Fri 09/09/11														
79	Management Plan	13 wks	Mon 12/12/11	Mon 19/03/12	78FS+													
80	Nooneys	130 days	Mon 02/04/12	Fri 28/09/12														
81	Site Survey	13 wks	Mon 02/04/12	Fri 29/06/12														
82	Management Plan	13 wks	Mon 02/07/12	Fri 28/09/12	81													
83	POND CREATION	556 days	Fri 15/01/10	Mon 12/03/12														
84	Dale Road Park (Spondon)	389.5 days	Fri 15/01/10	Thu 14/07/11														
85	Site Survey	0.5 days	Fri 15/01/10	Fri 15/01/10														
86	Create Pond Topology	1 wk	Fri 15/01/10	Fri 22/01/10	85													

Project: Project Plan v1.0R
Date: Mon 12/12/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			


WILD ABOUT PONDS
(SITA Project No.4770)

ID	Task Name	Duration	Start	Finish	Pred	2010				2011				2012				2013
						Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
87	Fence Off Old Pond	1 day	Fri 23/04/10	Fri 23/04/10	86													
88	Dig New Pond & Lay Pipework	1 wk	Mon 26/04/10	Fri 30/04/10	87													
89	Review Movement Process	0.33 days	Mon 11/10/10	Mon 11/10/10	88													
90	Move Plants and Beasities #1	1 day	Thu 14/10/10	Thu 14/10/10	89													
91	Move Plants and Beasities #2	1 day	Tue 19/10/10	Tue 19/10/10	90													
92	Dig Out Old Pond	1 day	Fri 29/10/10	Mon 01/11/10	91FS+													
93	Re-Site Spoil on Park	1 day	Tue 09/11/10	Tue 09/11/10	92FS+													
94	Remove Re-Emergent Plants	0.5 days	Thu 14/07/11	Thu 14/07/11	93													
95	Elm Wood LNR	403 days	Fri 15/01/10	Tue 02/08/11														
96	Site Survey	0.5 days	Fri 15/01/10	Fri 15/01/10														
97	Create Pond (x2) Topology	2 wks	Fri 15/01/10	Fri 29/01/10	96													
98	Procure Liners (x2)	2 wks	Wed 17/03/10	Tue 30/03/10	97FS+													
99	Dig New Pond & Remove Hazels	2 days	Wed 31/03/10	Thu 01/04/10	98,97													
100	New Pond Bank Topologies (x2)	1 day	Tue 02/08/11	Tue 02/08/11	99													
101	Alvaston Park	459 days	Tue 01/06/10	Mon 12/03/12														
102	Site Survey	0.5 days	Tue 01/06/10	Tue 01/06/10														
103	Create Pond Topology	2 wks	Tue 01/06/10	Tue 15/06/10	102													
104	School/Community Engagement	2 wks	Wed 01/09/10	Tue 14/09/10	103													
105	Confirm Wildlife Pond Site	0.5 days	Mon 20/12/10	Mon 20/12/10	104													
106	Dig New Wildlife Pond	4 days	Thu 03/02/11	Tue 08/02/11	105													
107	Open Tree Canopy	5 days	Mon 05/03/12	Fri 09/03/12	106													
108	Line New Pond	1 day	Mon 12/03/12	Mon 12/03/12	107													
109	Arboretum Park	165 days	Wed 01/09/10	Tue 19/04/11														
110	Site Survey	0.5 days	Wed 01/09/10	Wed 01/09/10														
111	Create Pond Topology	2 wks	Wed 01/09/10	Wed 15/09/10	110													
112	School/Community Engagement	1 day	Wed 15/12/10	Wed 15/12/10	111													
113	Dig New Pond	26 days	Tue 11/01/11	Tue 15/02/11	112													
114	Repair New Pond	1 day	Tue 19/04/11	Tue 19/04/11	113													
115	Derby Moor School	61.5 days	Mon 01/11/10	Tue 25/01/11														
116	School/Community Engagement	2 wks	Mon 01/11/10	Fri 12/11/10														
117	Site Survey	0.5 days	Mon 10/01/11	Mon 10/01/11	116													
118	Create Pond Topology	2 wks	Mon 10/01/11	Mon 24/01/11	117													
119	Dig New Pond	1 day	Mon 24/01/11	Tue 25/01/11	118													
120	POND RESTORATION	686 days	Fri 15/01/10	Mon 10/09/12														
121	Allestree Park Lake	300 days	Fri 15/01/10	Thu 10/03/11														
122	Site Survey	0.5 days	Fri 15/01/10	Fri 15/01/10														
123	Produce Costed Work Spec	10 days	Fri 15/01/10	Fri 29/01/10	122													
124	Agree Work Specification	20 days	Fri 29/01/10	Fri 26/02/10	123													
125	Procure Materials	15 days	Fri 26/02/10	Fri 19/03/10	124													
126	Implement Work (Phase 1)	3 days	Tue 23/03/10	Thu 25/03/10	125													
127	Implement Work (Phase 2)	2 days	Tue 30/03/10	Wed 31/03/10	126													
128	Willow Revetments Phase 2	44 days	Mon 10/01/11	Thu 10/03/11	127													
129	Allestree - Burley Brook	25 days	Mon 05/04/10	Fri 07/05/10														

Project: Project Plan v1.0R
Date: Mon 12/12/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			


WILD ABOUT PONDS
(SITA Project No.4770)

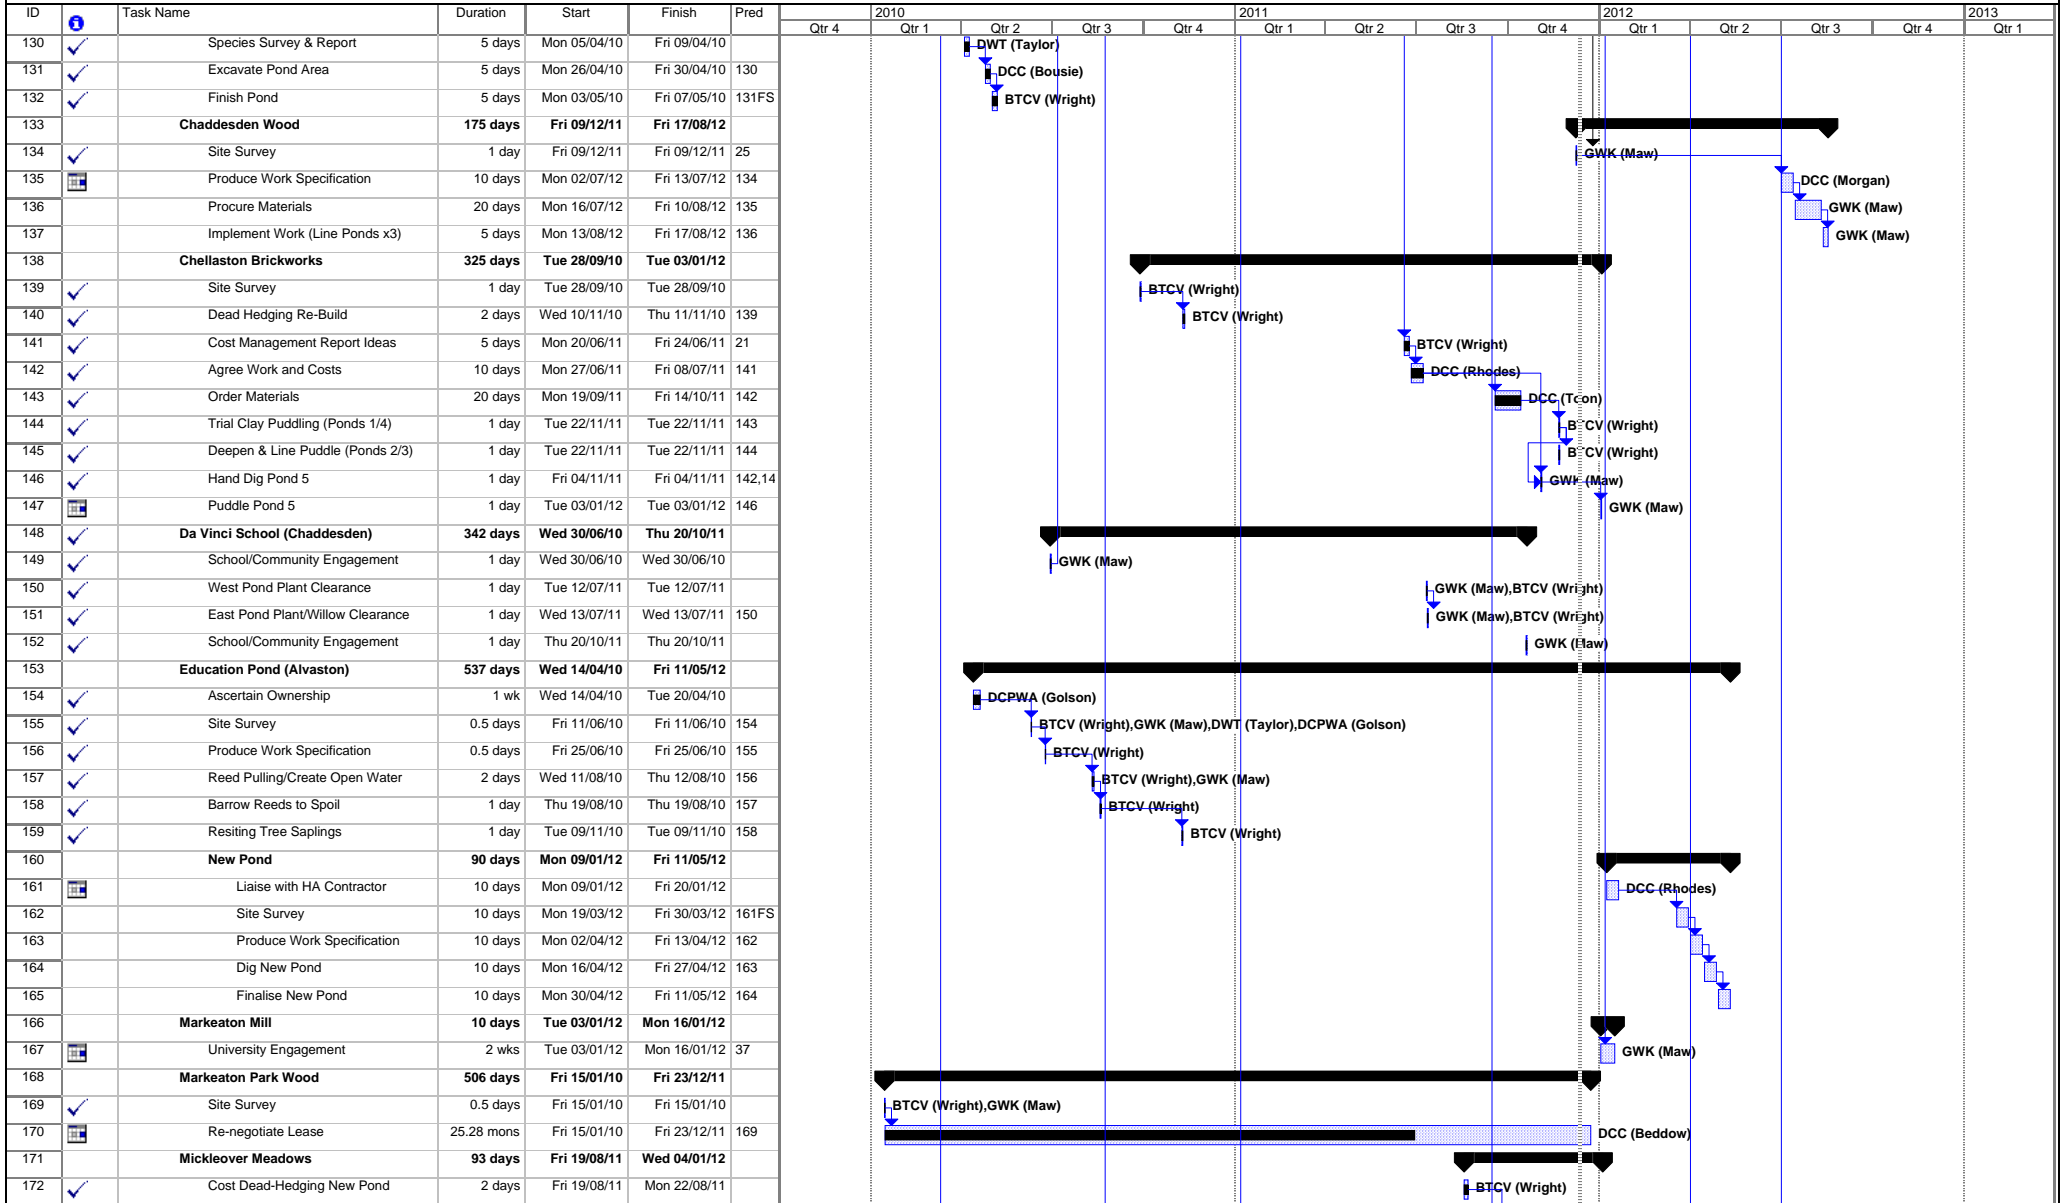

Project: Project Plan v1.0R
Date: Mon 12/12/11

Task Progress Summary External Tasks Deadline Split Milestone Project Summary External Milestone

WILD ABOUT PONDS
(SITA Project No.4770)

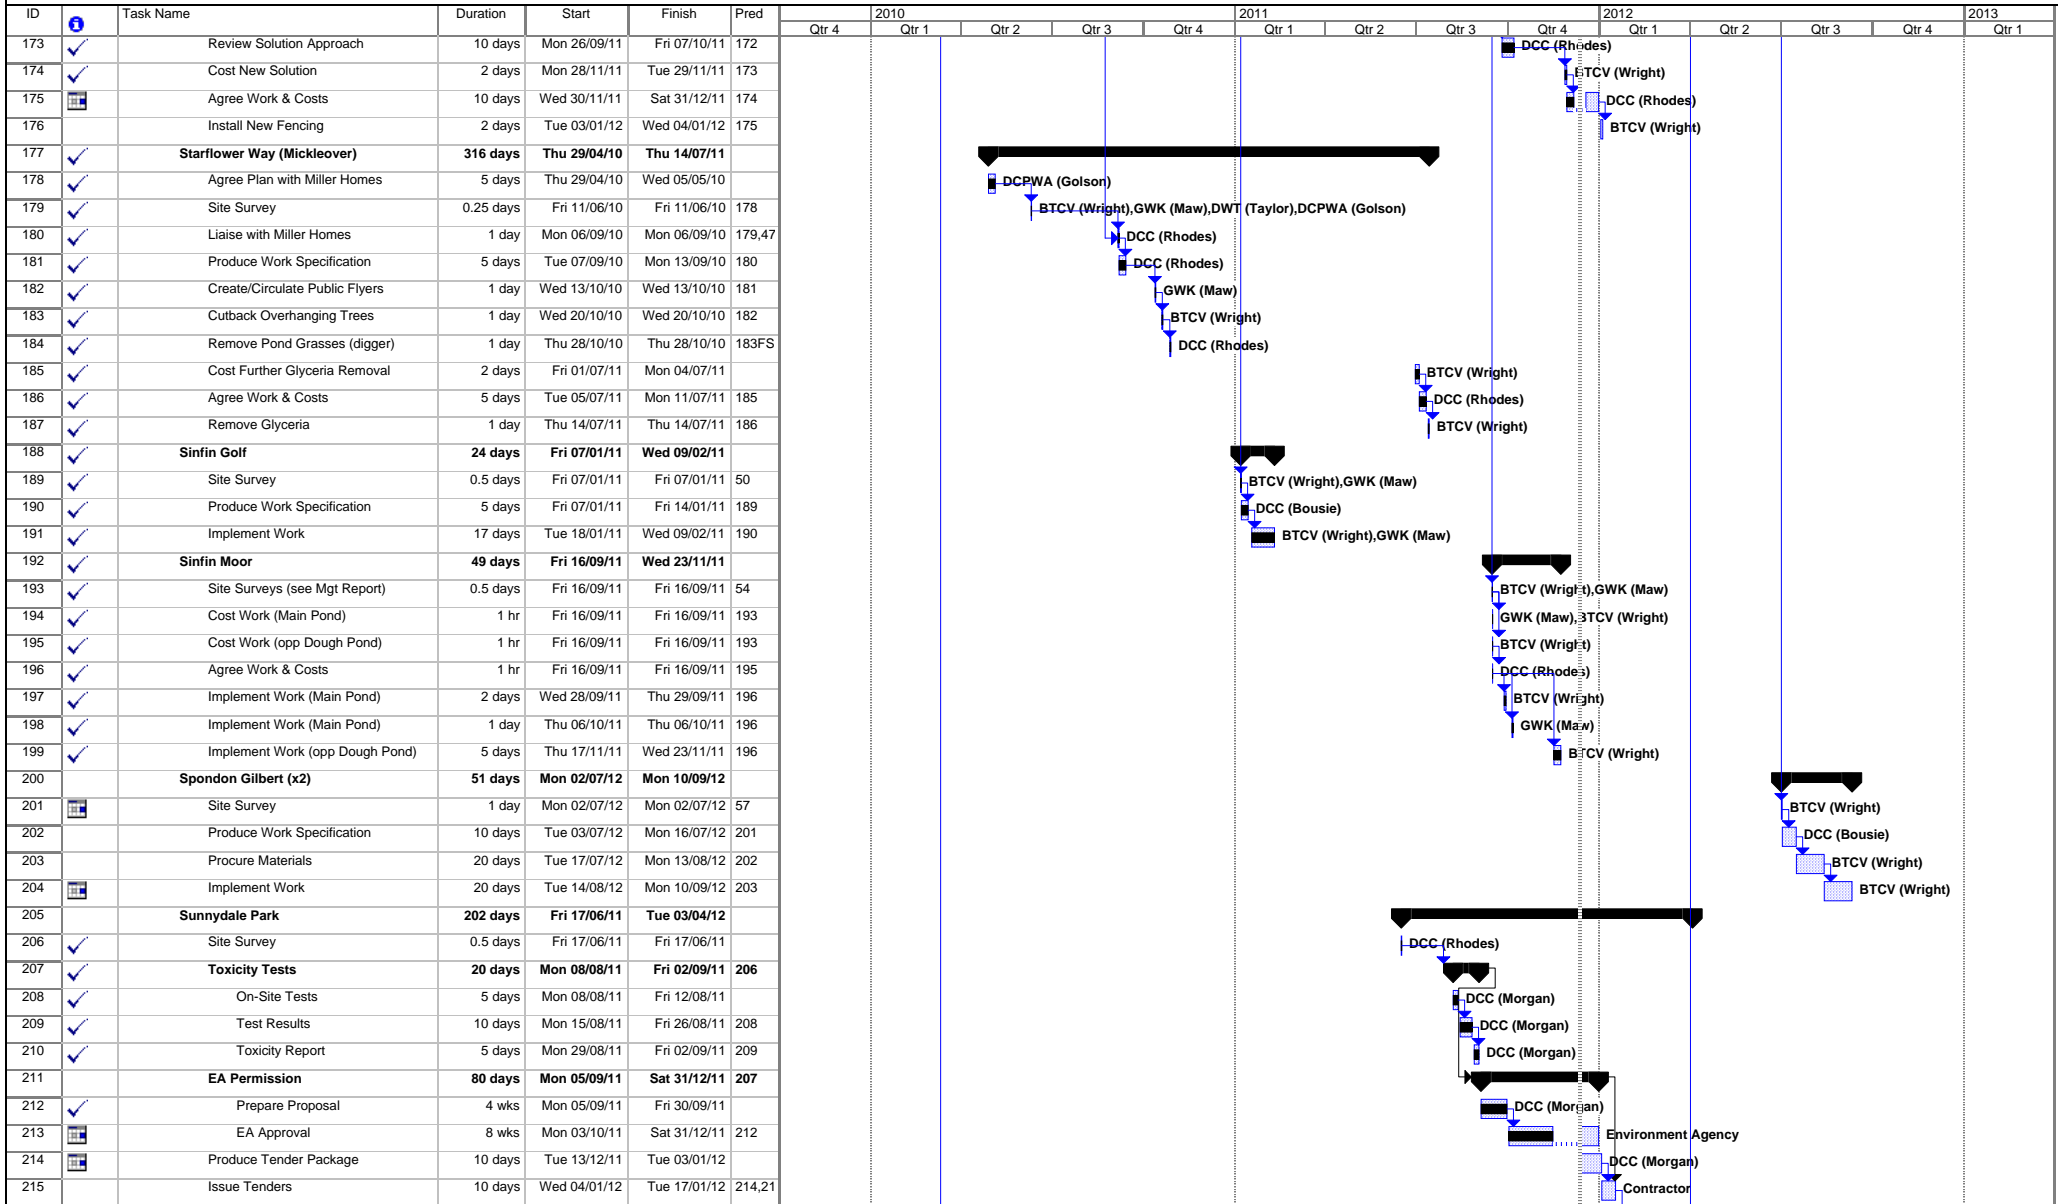

Project: Project Plan v1.0R
Date: Mon 12/12/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

WILD ABOUT PONDS
(SITA Project No.4770)

ID	Task Name	Duration	Start	Finish	Pred	2010				2011				2012				2013	
						Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
216	Awarded Desilting Contract	10 days	Wed 18/01/12	Tue 31/01/12	215														
217	Re-direct Brook	5 days	Wed 01/02/12	Tue 07/02/12	216														
218	De-Silt Existing Pond	1 wk	Wed 08/02/12	Tue 14/02/12	217														
219	Transfer Spoil to Park	1 wk	Wed 22/02/12	Tue 28/02/12	218FS														
220	Fence Off Spoil	1 day	Wed 29/02/12	Wed 29/02/12	219														
221	Spread Dried Spoil on Park	1 wk	Wed 28/03/12	Tue 03/04/12	219FS														
222	CRAYFISH	42 days	Wed 01/09/10	Thu 28/10/10															
223	Bramble Bank	42 days	Wed 01/09/10	Thu 28/10/10															
224	Site Survey	2 days	Wed 01/09/10	Thu 02/09/10															
225	Management Plan	8 wks	Fri 03/09/10	Thu 28/10/10	224														
226	Heatherton	40 days	Fri 03/09/10	Thu 28/10/10															
227	Site Survey	2 days	Fri 03/09/10	Mon 06/09/10	224														
228	Management Plan	7.6 wks	Tue 07/09/10	Thu 28/10/10	227														
229	The Sanctuary	38 days	Tue 07/09/10	Thu 28/10/10															
230	Site Survey	1 day	Tue 07/09/10	Tue 07/09/10	227														
231	Management Plan	7.4 wks	Wed 08/09/10	Thu 28/10/10	230														
232	MANAGEMENT REPORTING & BARS	790 days	Fri 01/01/10	Fri 18/01/13															
233	Project Launch Event (Allestree Park)	1 day	Thu 25/03/10	Thu 25/03/10	126SS														
234	Quarterly 1 Report	13 wks	Fri 01/01/10	Thu 01/04/10															
235	Quarterly 1 Newsletter	13 wks	Fri 01/01/10	Thu 01/04/10															
236	Quarterly 2 Report	13 wks	Fri 02/04/10	Thu 01/07/10	234														
237	Quarterly 2 Newsletter	13 wks	Fri 16/04/10	Thu 15/07/10	235FS														
238	Quarterly 3 Report	13 wks	Fri 02/07/10	Thu 30/09/10	236														
239	Quarterly 3 Newsletter	13 wks	Fri 16/07/10	Thu 14/10/10	237														
240	Quarterly 4 Report	13 wks	Fri 01/10/10	Thu 30/12/10	238														
241	Quarterly 4 Newsletter	13 wks	Fri 15/10/10	Thu 13/01/11	239														
242	Quarterly 5 Report	13 wks	Fri 31/12/10	Thu 31/03/11	240														
243	Quarterly 5 Newsletter	13 wks	Fri 14/01/11	Thu 14/04/11	241														
244	Quarterly 6 Report	13 wks	Fri 01/04/11	Thu 30/06/11	242														
245	Quarterly 6 Newsletter	13 wks	Fri 15/04/11	Thu 14/07/11	243														
246	Quarterly 7 Report	13 wks	Fri 01/07/11	Thu 29/09/11	244														
247	Quarterly 7 Newsletter	13 wks	Fri 15/07/11	Thu 13/10/11	245														
248	Quarterly 8 Report	13 wks	Fri 30/09/11	Fri 06/01/12	246														
249	Quarterly 8 Newsletter	13 wks	Fri 14/10/11	Fri 20/01/12	247														
250	Quarterly 9 Report	13 wks	Mon 09/01/12	Fri 06/04/12	248														
251	Quarterly 9 Newsletter	13 wks	Mon 23/01/12	Fri 20/04/12	249														
252	Quarterly 10 Report	13 wks	Mon 09/04/12	Fri 06/07/12	250														
253	Quarterly 10 Newsletter	13 wks	Mon 23/04/12	Fri 20/07/12	251														
254	Quarterly 11 Report	13 wks	Mon 09/07/12	Fri 05/10/12	252														
255	Quarterly 11 Newsletter	13 wks	Mon 23/07/12	Fri 19/10/12	253														
256	Quarterly 12 Report	13 wks	Mon 08/10/12	Fri 04/01/13	254														
257	Quarterly 12 Newsletter	13 wks	Mon 22/10/12	Fri 18/01/13	255														

Project: Project Plan v1.0R
Date: Mon 12/12/11

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
